

CONNECTIONS

Recycled Water Project Update

Redwood City Recycled Water Project — Seaport Area

February 2008

Seaport Area Pipeline Construction Update

Pipeline construction activity is subject to changes in weather conditions.

Seaport Court, Herkner Road and Seaport Blvd northeast of Chesapeake Drive (Bid Package No. 5)


The Bid Package No. 5 Recycled Water Pipeline installation is complete. Testing of the system and minor repairs are underway. The final paving operation will take place in February pending allowable weather conditions for asphalt placement.

Chesapeake Drive and Seaport Center Loop (Bid Package No. 6)

Bid Package No. 6 will be the next area of recycled water pipeline construction. The Contractor is anticipating a late February or early March start date pending cooperative weather conditions and the completion of startup activities.

Chesapeake Drive access will be maintained throughout the duration of the Project. A Project Informational meeting to provide businesses with project information will be held in the vicinity prior to construction starting. An announcement will be broadly distributed and emailed.

Construction work hours will be from 7:30 AM – 4:30 PM, Monday through Friday.

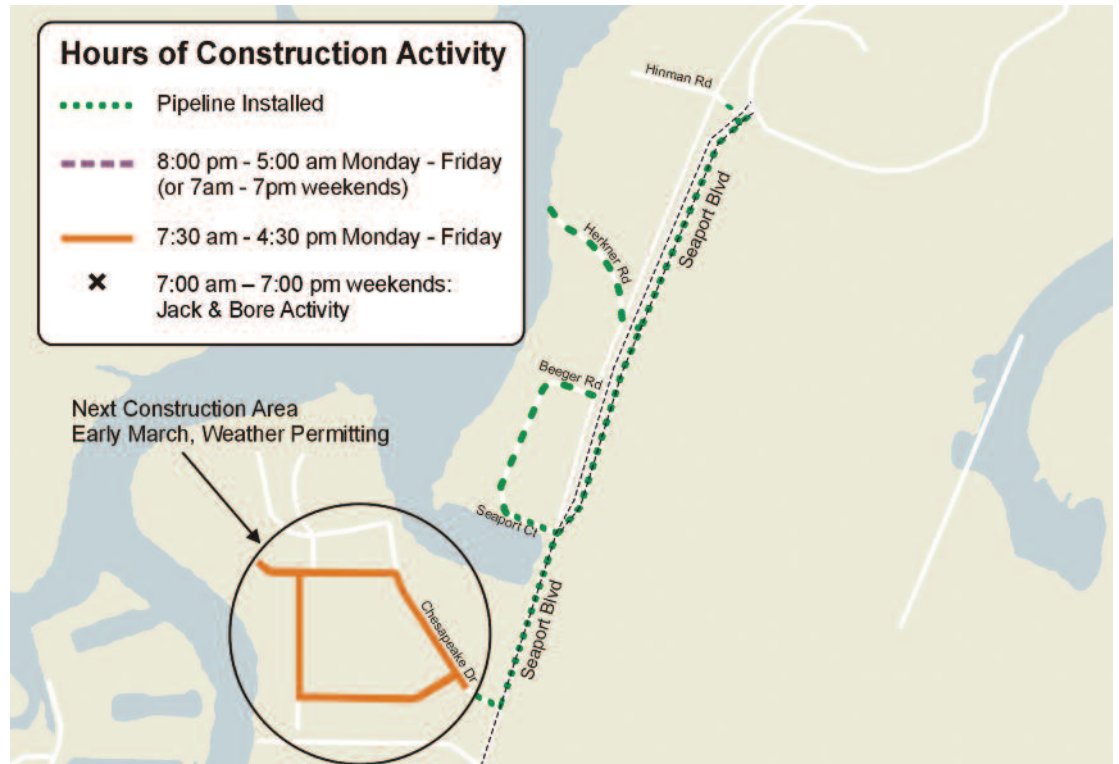

Map shows area under construction for the month of February 2008.

The City of Redwood City would like to thank you for your patience throughout construction of the Recycled Water Project. We are working closely with our contractors to minimize construction impacts. The project team is also working with local and regional fire and medical authorities to ensure that emergency access is not hindered by construction.

For Project Information

Please visit our project Web site at www.RedwoodCity.org/RecycledWater or call (650) 743-5759. If you'd like to have Project Updates emailed to you, please send an email to SeaportUpdates@DataInstincts.com.



Project Information Resources:
(650) 743-5759

SeaportUpdate@DataInstincts.com
www.RedwoodCity.org/RecycledWater
