

CONNECTIONS

Recycled Water Project Update

Redwood City Recycled Water Project

April 2006

Pipeline Construction Activity Begins


Construction Will Begin on Redwood Shores Parkway and Radio Road

Pipeline construction will begin in April near the intersection of Shearwater and Redwood Shores Parkways, then proceeding onto Radio Road toward the South Bayside System Authority (SBSA) Treatment Plant site. Mitchell Engineering was awarded the construction contract for installing recycled water pipelines in Bid Package #1, which includes this section as well as a mile plus section along the eastern end of Marine Parkway from Shearwater Parkway to just past Bridge Parkway.

During the first week of April, you will see work crews conducting surveys and marking underground utility locations and the new pipeline alignments, as well as beginning to cut pavement and conducting exploratory potholes to locate major underground utilities. Following that work, you can expect to see construction equipment assembling and materials being delivered to the vicinity. Once construction activities fully commence, there will be signs, barricades and construction cones clearly identifying the construction zone as it progresses along the affected streets.

Construction along Redwood Shores Parkway and Radio Road is expected to continue through May, and traffic will be limited to one lane in areas of construction. Flaggers will be present to direct traffic one direction at a time. Please allow for brief delays when commuting along this section of Redwood Shores Parkway and Radio Road. Construction hours are from 7:30 AM to 4 PM, weekdays only. Construction on Marine Parkway is expected to begin as early as May and advance notice will be provided.

The next package of pipelines in Redwood Shores, which includes

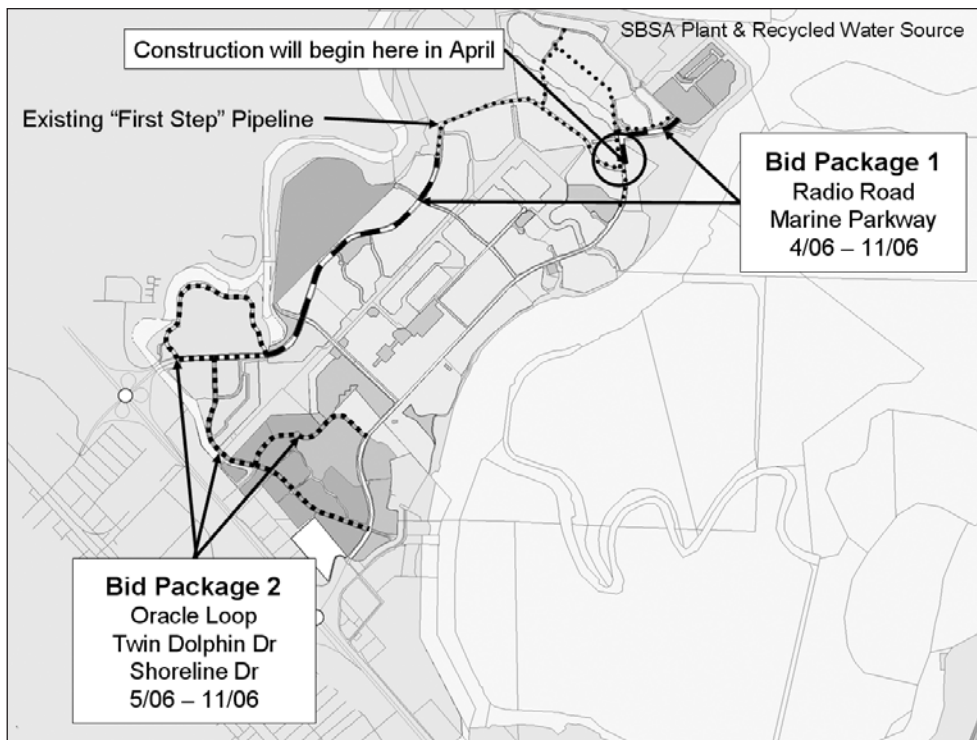

2006 construction will begin in April and end in November. There will be a few construction crews, completing short sections of the pipeline at a time, moving along the streets shown here.

the remainder of Marine Parkway to Oracle Parkway, the loop around Oracle, Twin Dolphin Drive and Shoreline Drive, was recently awarded to the construction firm, K.J. Woods Construction Inc. That work is expected to begin in May, and continue through November 2006.

Construction details will be updated frequently. The best way to get the most current information is to send an email to RCconstruction@DataInstincts.com to receive emailed project updates and to look for updated information in next month's Pilot. Call (650) 743-5759 if you have specific questions or concerns.

SBSA Construction Update Pile Driving to Resume

Within the first two weeks of April, you can expect about six working days of sheet pile driving. The Contractor will be installing 25-foot long sheet piles. These piles are much shorter than those previously used, so the resulting duration and intensity of noise will be less than what occurred last fall. We will be sending an email notice prior to this activity once the exact dates are known.

Also, the 65-foot sheet piles that were driven in last year will be removed from a portion of the facility. The walls of the facility have been completed in some areas, and the sheet piles are no longer needed to hold back the bay mud. This work will also involve some intermittent noise for short periods of time.

Upcoming Events

- **April 24:** City Council to review the Cross Connection Prevention Program and Treatment Performance Monitoring Program



Project Information Resources:
(650) 743-5759

RCconstruction@DataInstincts.com
www.RedwoodCity.org/RecycledWater
