

CONNECTIONS

Recycled Water Project Update

Redwood City Recycled Water Project

August 2006

Recycled Water Pipeline Installation Continues

Marine Parkway


Main pipeline work on Marine Parkway will be completed by early August. Final connections and testing will continue in various locations throughout the month. Initial pavement repairs and smoothing of the road surface will also be ongoing during August. Final resurfacing will occur next Spring. Construction hours will occur between 7:30 AM and 4:00 PM. Traffic flow will be maintained, but there may be minor delays. Look for lane changes with traffic cones and flagmen in the narrower sections along Marine Parkway.

Twin Dolphin Drive

During most of August, pipeline installation will be on Twin Dolphin Drive, in the north-bound lanes, moving from Shoreline Parkway toward Redwood Shores Parkway. After the main pipeline is completely installed, valves, services and accessories will be installed along the entire length of Twin Dolphin. Traffic will be detoured on these roads, usually to other lanes along Twin Dolphin Drive. Please watch for lane changes, alternate driveway access/egress, barricades, cones and flagmen directing traffic during construction periods. Working hours for these segments will be between 7:30 AM and 4:00 PM and traffic flow will be maintained.

Shoreline Parkway

Pipeline installation along Shoreline Parkway may begin by the end of August. Because of the narrow and curved roadway, traffic will be diverted between breaks in the islands, so please look for lane detours, changes, alternate driveway access/egress,

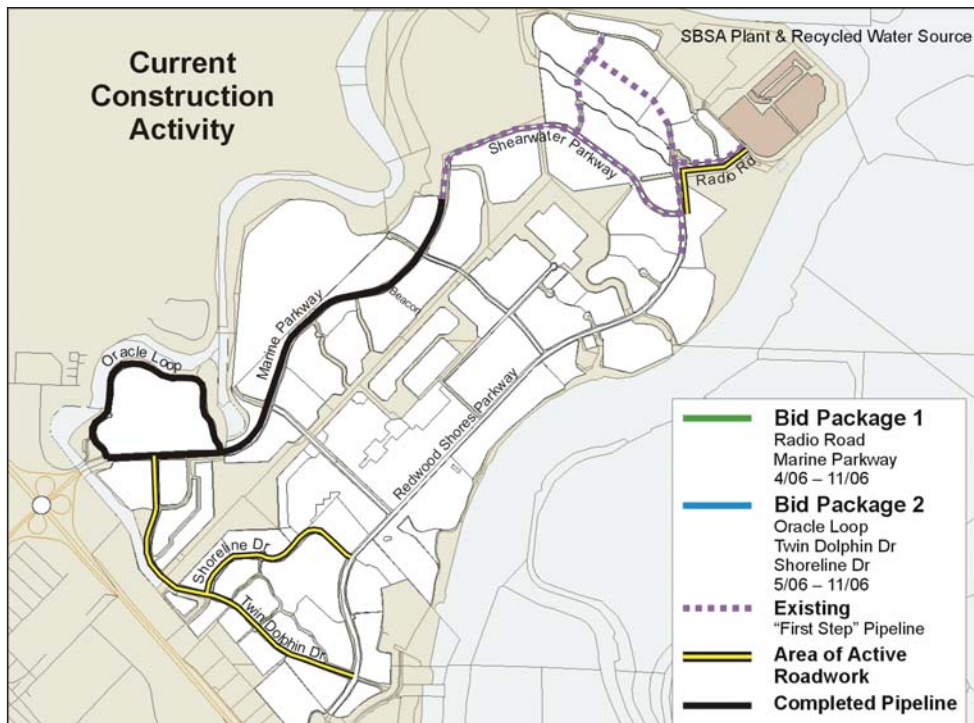

Pipe installation crews are active in two locations. About 21,000 of 27,000 linear feet of the first year pipeline installation has been completed.

barricades, cones and flagmen directing traffic during construction periods. Working hours for this segment will be between 7:30 AM and 4:00 PM and traffic flow will be maintained.

Redwood Shores Parkway and Radio Road

Installation of recycled water pipeline will continue along parts of Redwood Shores Parkway and Radio Road near the new SBSA Treatment Plant. After the main pipelines are completely installed, valves and accessories will be installed along with other structures. Once the pipeline is tested, pavement repairs and smoothing of the road surface will occur. Final resurfacing will occur next Spring.

SBSA Update

More concrete work will occur in August, and the main activity will be completing the walls for holding tanks and floor slabs. The steel sheet piles that have provided a temporary wall for the storage tanks will be

removed at the end of August or first week of September. This is the only activity that may have noise associated.

Construction details are updated frequently. If you have specific questions or concerns, call (650) 743-5759, or send an email to RCConstruction@DataInstincts.com to receive emailed project updates.



Project Information Resources:
(650) 743-5759

RCConstruction@DataInstincts.com
www.RedwoodCity.org/RecycledWater
