

CONNECTIONS

Recycled Water Project Update

Redwood City Recycled Water Project

June 2006

Construction Continues on Redwood Shores Parkway and Radio Road

Construction continues on the first of two pipelines along Redwood Shores Parkway and Radio Road toward the new SBSA Treatment Plant site. Work will continue along Radio Road and then shift back to Redwood Shores Parkway to finish the first line. About mid-June, construction on the second line on Redwood Shores Parkway will begin, headed toward the SBSA Treatment Plant.


During construction activities, traffic along Redwood Shores Parkway and Radio Road will be limited to one lane in areas of construction. Temporary traffic signals, flaggers, barricades and delineators will direct traffic in one direction at a time. Please allow for brief delays when commuting along this section of Redwood Shores Parkway and Radio Road. Construction hours are from 7:30 AM to 4 PM, weekdays only.

Construction Begins on Marine and Oracle Parkways

Full construction activities will begin in early June on Marine Parkway. Advance notices will be provided by K.J. Woods Construction. They will begin pipeline installation at the western end of Marine Parkway and work between Twin Dolphin and Oracle Parkway East. Working hours here will be 7:30 AM to 4:00 PM. When completed with this section, they will move between Twin Dolphin and Oracle Parkway West. Working hours for this high-traffic section will be from 10:00 AM to 4:00 PM in order to avoid the busiest part of rush hour. The intersection work at Marine Parkway and Oracle Parkway West will be conducted at night between 8 PM and 6 AM. Work will then proceed around the Oracle loop between 7:30 AM to 4:00 PM.

Mitchell Engineering will also start construction activities in June starting east of Island Parkway and moving further toward the eastern end of Marine Parkway. Working hours here are between 7:30 AM and 4:00 PM.

The majority of the work for all crews on Marine Parkway, except for intersections, will be done in the inbound (eastern) direction lanes.

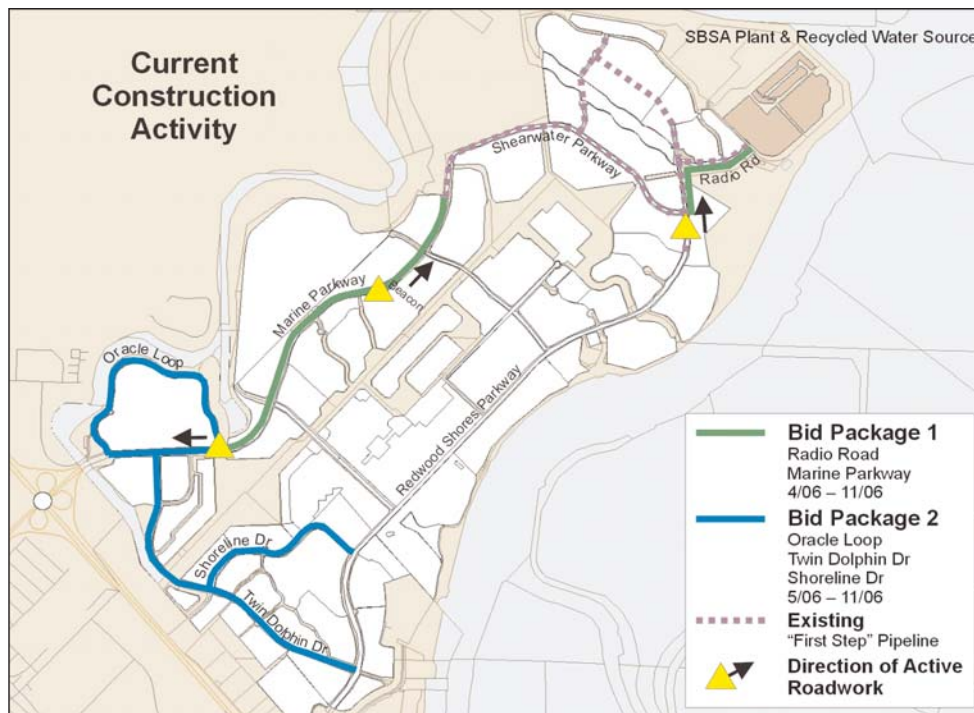

Pipe installation crews are active in three locations.

Construction zones will be clearly marked by barricades and delineators and traffic direction will be provided.

Ensure There is NO Interruption to Your Data Lines During Construction

Before construction begins, the City and utility providers locate and mark reported data lines within the public utility easement. It is the contractor's responsibility to respect these markings during pipeline construction. If you have fiber optic cables or data lines that you believe may not have been reported to the Underground Services Alert (USA), please contact either Phong Du at (650) 780-7385 or Mark Millan at (650) 743-5759. Or, notify us as to who your provider is so verifications can be made.

SBSA Concrete Work

Concrete work continues at SBSA during the month of June. The walls of the storage tanks are complete, and concrete work to form the roof over the tanks is expected to begin. Consistent with previous concrete work, this is a little to no noise impact activity.

Construction details are updated frequently. If you have specific questions or concerns, call (650) 743-5759, or send an email to

RCConstruction@DataInstincts.com to receive emailed project updates.

Don't Forget to Get Your FREE Low Flow Toilet!

Help save up to 100 million gallons of water annually! Redwood City's Toilet Replacement Program offers free replacement of old water-wasting toilets with high-efficiency models that utilize state-of-the-art technology (with tested and proven high flushing performance) for single-family, multi-family, and commercial customers — and installation is free, too. To participate in this program, visit http://www.redwoodcity.org/publicworks/water/water_conservation.htm to get an application. You'll be saving water and money, while you help preserve our community's water supply!



Project Information Resources:
(650) 743-5759

RCConstruction@DataInstincts.com
www.RedwoodCity.org/RecycledWater
