

CONNECTIONS

Recycled Water Project Update

Redwood City Recycled Water Project

May 2006

After a Wet April, Pipeline Construction Gets Underway in May

Potholing and Surveying Activity

May will see potholing and surveying along sections of Marine Parkway and the Oracle loop. Surveying and potholing began the last week of April on Marine Parkway and will continue through May in sections between Shearwater to Highway 101 and along the Oracle Parkway loop.


During the second half of May, you may begin to see excavation and pipe-laying between Beacon Parkway and Shearwater, along Marine Parkway. When construction on Marine Parkway is about to begin, door-hanger notices will be distributed in advance by the contractor, Mitchell Engineering. Construction zones will be clearly marked by barricades and delineators and traffic direction will be provided by flaggers.

Pipe-laying Activity

The pipe-laying activity will continue along Redwood Shores Parkway near Radio Road and on Radio Road. During construction activities, traffic will be limited to one lane in areas of construction. Flaggers, barricades and delineators will direct traffic one direction at a time. Temporary traffic signals will be used in this section. The light signals will be timed to optimize the flow of traffic and will move with work crews.

Construction equipment and materials will remain to the side of the road at night and during non-construction hours and will also be surrounded by construction cones and/or barricades. Construction hours are from 7:30 AM to 4 PM, Monday through Friday. Please allow for brief delays when commuting along this section of Redwood Shores Parkway and Radio Road.

Construction details will be updated frequently. The best way to get the most current information is to send

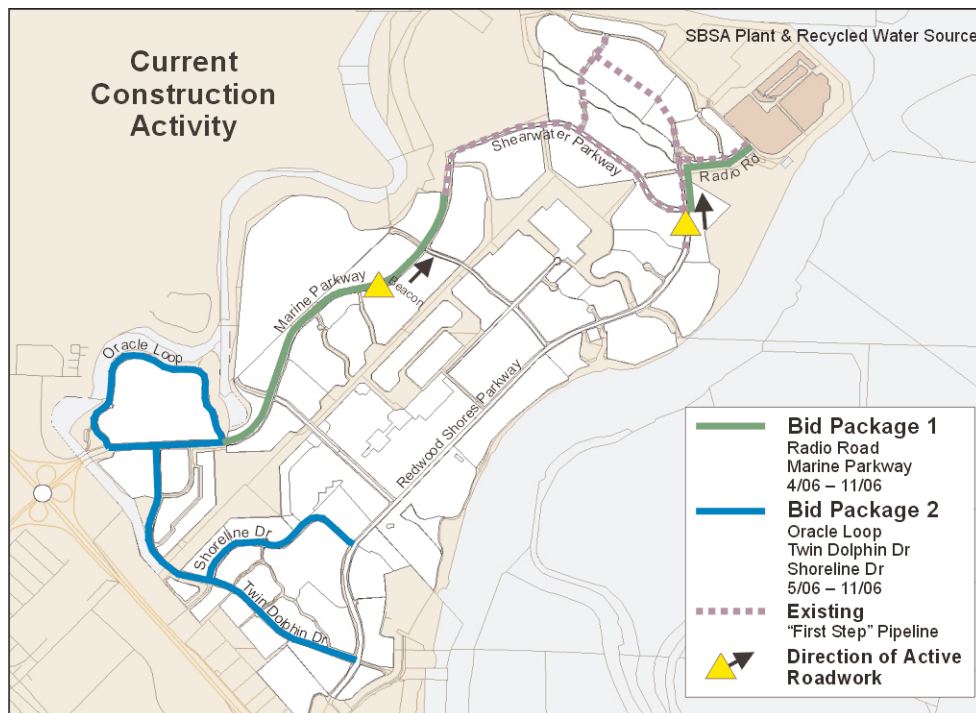

Pipe-laying work is expected to begin in May along Redwood Shores Parkway and Marine Parkway.

an email to RCConstruction@DataInstincts.com to receive emailed project updates. Call (650) 743-5759 if you have specific questions or concerns.

SBSA Construction Update

May's construction activities at the SBSA construction site will focus on completing the disinfection tanks. The concrete walls of these tanks are about 2/3 completed, and the main activities will be excavation and concrete work. The recycled water lines coming from the new facility to Radio Road are also being installed. In addition, the 65-foot sheet piles that were holding the pump station up will be removed for during a two-day span within the second or third week of May. Some noise will occur from the vibratory hammer, as was heard in the third week of April.

Water Conservation Update

Attend Our Water Wise Spring Gardening Workshops
Redwood City invites you to attend one or all of their FREE Water Wise Spring Gardening Workshops, held on Saturdays:

- May 6: Irrigation Basics
9:00 AM to 12:30 PM
- May 6: Smart Gardening
1:30 to 5:00 PM

- May 13: ET Controller Concepts
9:00 AM to 12:30 PM
- May 20: Irrigation Scheduling/
Maintenance
9:00 AM to 12:30 PM
- May 20: Smart Gardening (repeat)
1:30 to 5:00 PM

All workshops will take place at:
Redwood City Hall, Council
Chambers, 1017 Middlefield Road

For more information on the content of these workshops or to submit your RSVP online, please visit www.RedwoodCity.org/Conservation. To reserve your place to attend any workshop, you may also call (650) 780-7436. Walk-ins are welcome, although we encourage reservations to ensure adequate materials are available.



Project Information Resources:
(650) 743-5759
RCConstruction@DataInstincts.com
www.RedwoodCity.org/RecycledWater
