

CONNECTIONS

Recycled Water Project Update

Redwood City Recycled Water Project

October 2006

Season One Pipeline Installation Nearing Completion

Marine Parkway

Main pipeline work on the western end of Marine Parkway is completed, including most pavement repairs. Work to restore the traffic signal loops will be done within the first two weeks of October. However, laterals (smaller piping that connects individual customers to the main line) crossing Marine Parkway, final connections and testing will continue in various locations throughout the month along the eastern part of Marine Parkway. Construction hours will occur between 7:30 AM and 4:00 PM. Traffic flow will be maintained, but there may be minor delays. Please look for lane changes with traffic cones and flagmen in the narrower sections along the eastern part of Marine Parkway. Once laterals and testing are completed in this section, pavement repairs will follow.

Oracle Parkway


Pipeline work is complete on Oracle Parkway and pavement repairs are underway, which should be completed in the first week of October.

Twin Dolphin Drive and Shoreline Parkway

Main pipeline work has been completed and final construction pavement repairs are underway. They should be completed during the first week or two of October.

Redwood Shores Parkway and Radio Road

Installation of recycled water pipeline will continue through part of October

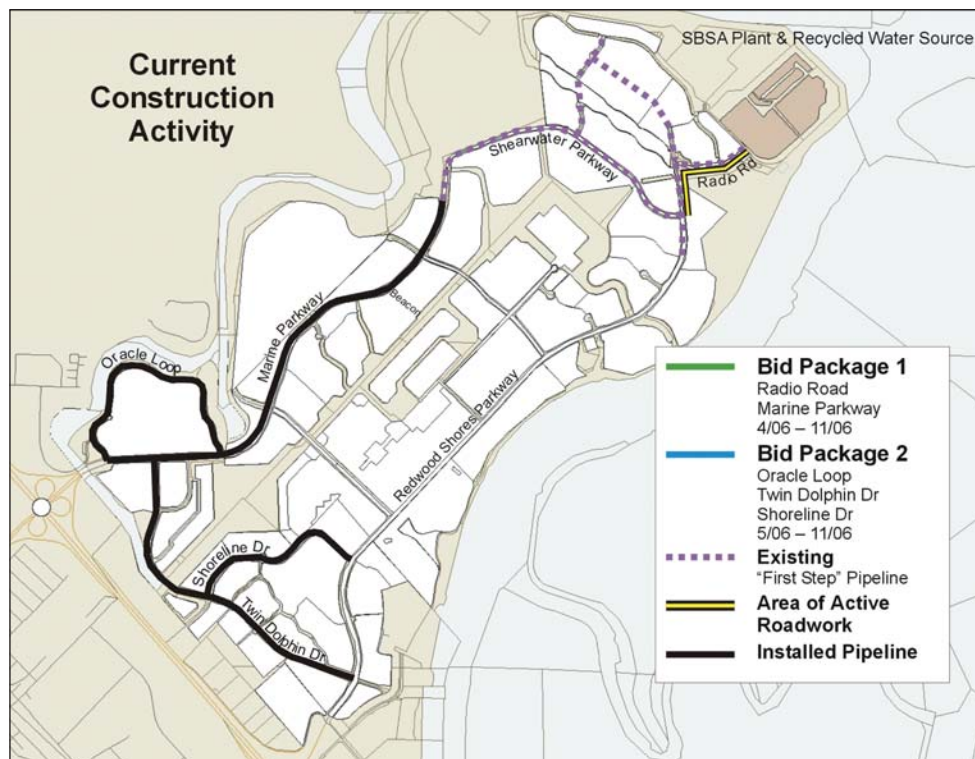

Pipe installation crews are active on (Radio Road and Redwood Shores Parkway) with smaller crews in other locations. Just over 26,000 of 27,000 linear feet of the first year pipeline installation has been completed.


along Radio Road near the new SBSA Recycled Water Facility and connecting segments on both Radio Road and Redwood Shores Parkway. After the main pipelines are completely installed, valves and accessories will be installed, along with final connections, testing and other structures on both Radio Road and Redwood Shores Parkway. Once the pipeline is tested and accepted, pavement repairs will be made to the road.

What condition will the roadways be left in?

Please be assured that the roadways where recycled water pipelines are being installed will be restored. Once

the testing is completed and approved for a given area, the next step in the road restoration process will include removing this temporary surface and installing a permanent asphalt pavement surface. This pavement will be a smooth, integrated surface, flush with the existing roadway and slightly wider than the original trench. This entire phase of work will be completed by the end of this year, but during the following construction season, Redwood City will recondition all the affected roadways to extend their useful life with a slurry seal coating. At that time new pavement markings, reflectors and striping will also be installed.

2007 Pipeline Construction

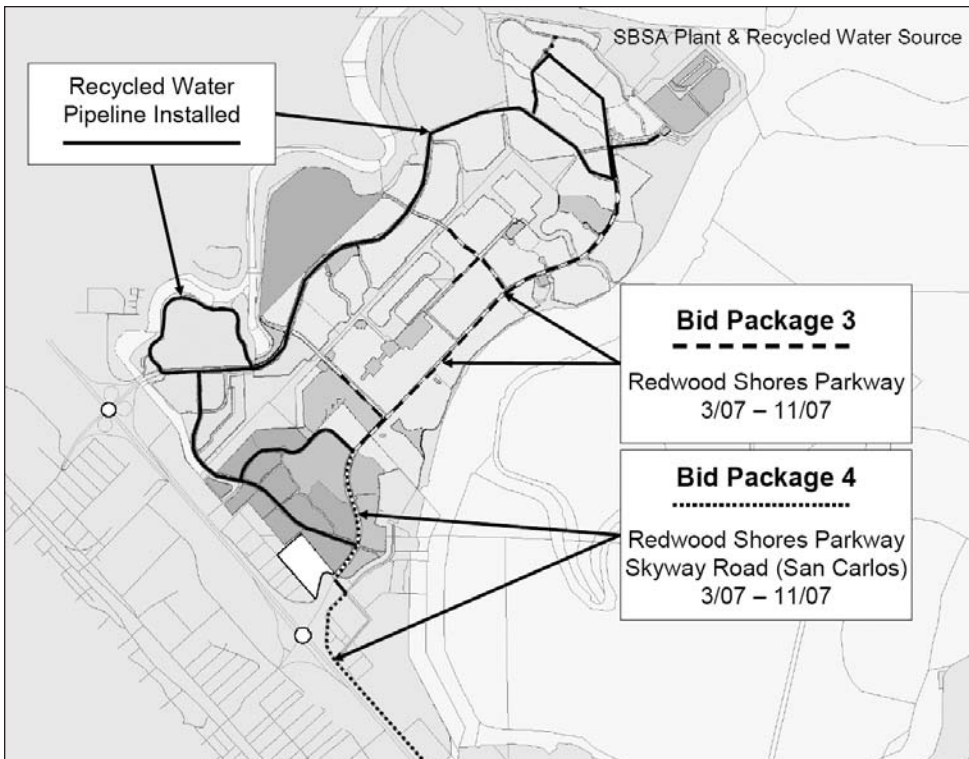

Bid Packages 3 and 4 will complete pipeline installation along sections of Redwood Shores Parkway, Skyway Road, Shell Parkway, Davit Lane, and Bridge Parkway. Preconstruction activity may happen in 2006, but main pipeline installation will occur in 2007.

In 2007, the City of Redwood City will be continuing work on its recycled water pipeline system along Redwood Shores Parkway and Skyway Road in the Redwood Shores area. The construction will include trenching in the streets and the installation of pipeline segments on Redwood Shores Parkway beginning at Shearwater Parkway southwest to Airport Way and continuing along Skyway Road (in San Carlos), with some sections of Shell Parkway, Davit Lane, and Bridge Parkway.

An informational Open House meeting will occur for residents and businesses in the area about one month before construction will begin. A notice will be sent out in advance with meeting details.

Your patience and understanding during construction has and will continue to be much appreciated through these next construction phases. Resurfacing over trenched areas will continue this fall for Radio Road and Marine Parkway. We will continue to do our best to minimize project-related disruptions during construction.

Information regarding construction progress, including detailed schedule information, will be posted on our project website at:
www.redwoodcity.org/RecycledWater

continued from page 1...

Should you experience any unsafe roadway conditions along the trenchline, please call the Project Hotline at (650) 743-5759 with specific details. Thank you for your patience and consideration during the construction of the Redwood City Recycled Water Project.

SBSA Work Soon to be Completed

In October, the concrete work will come to an end with the completion of the facility structure. Piping and electrical work will be ongoing on the interior of the facility in preparation for testing the storage and pumping system. There will continue to be activity on the outside of the structure as the area is prepared to receive landscaping.

Information regarding construction progress, including detailed schedule information, will be posted on our project website at:
www.redwoodcity.org/RecycledWater



Project Information Resources:
 (650) 743-5759

RCConstruction@DataInstincts.com
www.RedwoodCity.org/RecycledWater
