

# CONNECTIONS

## Recycled Water Project Update

Redwood City Recycled Water Project

July 2006

### Recycled Water Pipeline Installation Continues

#### Oracle/Marine Parkway

Now that pipeline installation has been completed along the Oracle Parkway loop, some follow up work will continue during July. Construction hours are from 7:30 AM to 4:00 PM. Traffic flow will be maintained, but there may be minor delays. Look for lane changes and flaggers in the narrower sections along Oracle Parkway. For more information on how the roadway will be renovated see below.

#### Twin Dolphin Drive

About mid July, pipeline installation will begin on Twin Dolphin Drive. Work will begin at its intersection with Marine Parkway, and move south along Twin Dolphin Drive. The intersection will be worked on during the hours of 10:00 AM and 4:00 PM, while the main roadway work will occur between 7:30 AM and 4:00 PM.

#### Marine Parkway


Pipeline installation is also underway along Marine Parkway between Oracle Parkway East and Beacon Shores.

#### Radio Road

There will be recycled water pipeline installation through July along the eastern end of Redwood Shores Parkway and Radio Road. Work will begin near the Shearwater Parkway intersection, and will continue east toward Radio Road and the SBSA Treatment Plant.

### What condition will the roadways be left in?

Please be assured that the roadways where recycled water pipelines are being installed will be restored. The trenchline is currently only covered with a temporary surface until the main pipeline and associated fixtures and fittings have passed the required system testing. Once the testing is completed and approved for a given area, the next step in the road restoration process will include removing this temporary surface and installing the permanent asphalt

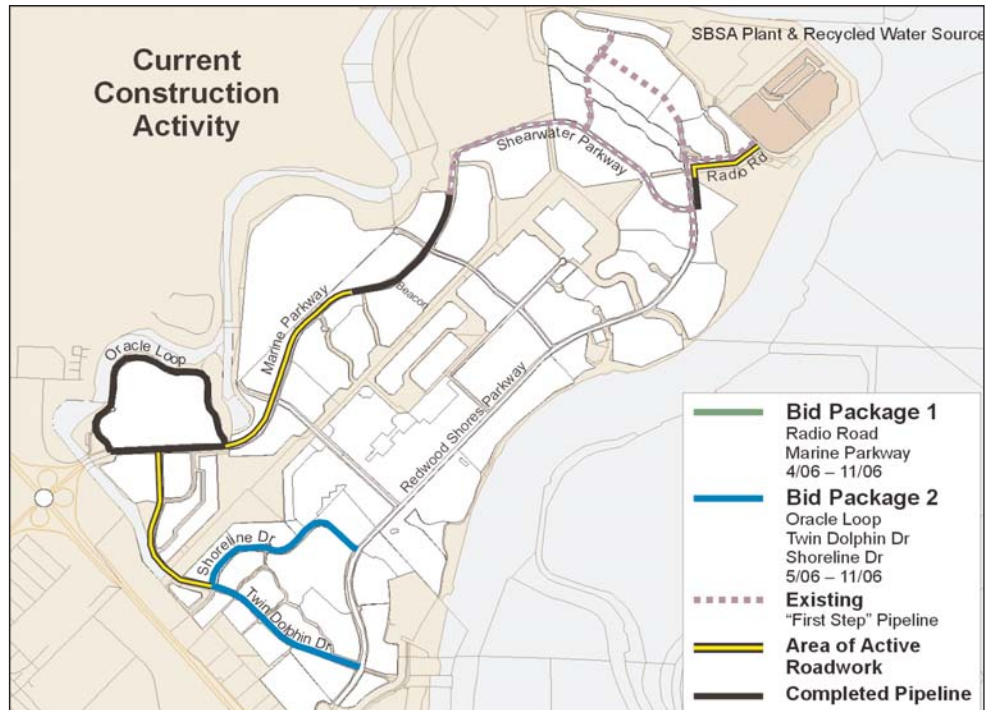

Pipe installation crews are active in three locations. About 12,500 of 19,000 feet of main line pipe has already been installed on Oracle Parkway, Marine Parkway, Radio Road, and Airport Way.

pavement surface per the engineering specifications. This pavement will be a smooth, integrated surface, flush with the existing roadway and slightly wider than the original trench. At that time, damaged lane markings will be replaced. This entire phase of work will be completed by the end of this year, but during the following construction season, Redwood City will recondition all the affected roadways to extend their useful life with a slurry seal coating. At that time new pavement markings, reflectors and striping will also be installed.

The project team is committed to restoring the roadway to its original, or in some instances, improved condition. Should you experience any unsafe roadway conditions along the trenchline, please call the Project Hotline at (650) 743-5759 with specific details. Thank you for your patience and consideration during the construction of the Redwood City Recycled Water Pipeline.

### SBSA Update – Concrete Work Continues

The forming of the concrete roofs for the new Storage tanks is underway. This is not a noise intensive task, and will continue through July.

Excavation for the electrical building that will be attached to the tank structure has begun. After excavation, work at this area will consist of placing rebar and concrete for the building slab. Simultaneously, in the area south of the new tanks, excavation for the last major portion of the new structure will begin with more rebar and concrete work to follow.

Construction details are updated frequently. If you have specific questions or concerns, call (650) 743-5759, or send an email to [RCConstruction@DataInstincts.com](mailto:RCConstruction@DataInstincts.com) to receive emailed project updates.



**REDWOOD CITY**  
RECYCLED WATER PROJECT  
A VALUABLE COMMUNITY RESOURCE

Project Information Resources:  
(650) 743-5759

[RCConstruction@DataInstincts.com](mailto:RCConstruction@DataInstincts.com)  
[www.RedwoodCity.org/RecycledWater](http://www.RedwoodCity.org/RecycledWater)
